Democratic Socialist Republic of Sri Lanka
MINISTRY OF TRANSPORT & HIGHWAYS
ROAD DEVELOPMENT AUTHORITY
BIDDING DOCUMENT
FOR
RECTIFICATION AND ASPHALT SURFACING ON AMPARA IGINIYAGALA ROAD FROM 11+500 TO 17+000 KM
CONTRACT NO. RDA/RM&M/EP(Akk)/RMI/2024/13
BID SUBMITTED BY
[Name of the Bidder]

CONTENTS

		Page
Project Location M	ар	03
Volume 1		05
Section 1	Instructions to Bidders	07
Section 3	Conditions of Contract	08
Section 5	Standard Forms - Contract	09
Volume 2		15
Invitation for	Bids	17
Section 2	Bidding Data	18
Section 4	Contract Data	24
Section 6	Specifications	32
Section 7	Form of Bid	48
Section 8	Bill of Quantities	49
Section 9	Schedules	60
Section 11	Standard Forms (Bid)	67
Section 10	Drawings	71
	COY	
0		

Project Location Map

Introduction

This Bidding Document has two parts, namely, Volume 1 and Volume 2.

The bidders are expected to buy the following Standard Bidding Document from the Construction Industry Development Authority (CIDA) (former ICTAD): -

STANDARD BIDDING DOCUMENT PROCUREMENT OF WORKS MAJOR CONTRACTS SECOND EDITION – JANUARY 2007 with addendum issued in October 2009 by ICTAD ICTAD PUBLICATION NO. – ICTAD/SBD/02

This Bidding Document shall be read in conjunction with the above Standard Bidding Document.

The Address of CIDA is

Construction Industry Development Authority 'Savsiripaya'123, Wijerama Mawatha, Colombo-07

VOLUME 1

VOLUME 1

- Section 1 Instruction to Bidders
- Section 3 Conditions of Contract
- Section 5 Standard Forms (Contract)

Section - 1

Instruction to Bidders

The text of this 'Instructions to Bidders' is found in the 'Standard Bidding Document Procurement of Works Major Contracts '

ICTAD Publication No. ICTAD/SBD/02 – Second Edition – January 2007 with Addendum issued in October 2009 by ICTAD

This publication is copyright and bidders, if they do not already possess a copy, may obtain it from:

Construction Industry Development Authority 'Savsiripaya' 123, Wijerama Mawatha Colombo-07

This has to be read in conjunction with Section 2 - 'Bidding Data of this Bidding Document. Wherever the Clauses of the Section 1 - 'Instruction to Bidders' have to be modified and/or supplemented, it is done through the text in the Section -2 - 'Bidding Data'.

Section - 3

Conditions of Contract

The text of this 'Conditions of Contract' is found in the

'Standard Bidding Document Procurement of Works Major Contracts'

ICTAD Publication No. ICTAD/SBD/02 – Second Edition – January 2007 with Addendum issued in October 2009 by ICTAD.

This publication is copyright and bidders, if they do not already possess a copy, may obtain it from:

Construction Industry Development Authority

'Savsiripaya'

123, Wijerama Mawatha

Colombo-07

This has to be read in conjunction with Section 4 - 'Contract Data' of this Bidding Document. Wherever the Clauses of the Section -3 – 'Conditions of Contract' have to be modified and/or supplemented, it is done through the text in the Section 4 – 'Contract Data'.

Section - 5

Standard Forms (Contract)

- Letter of Acceptance
- Performance Guarantee
- Form of Agreement
- Advance Payment Security
- Retention Money Guarantee

FORM OF LETTER OF ACCEPTANCE

[Date]

[Contractor's Name & Address]

This is to notify you that your bid dated for the construction and remedying the defects of the **'RECTIFICATION AND ASPHALT SURFACING ON AMPARA IGINIYAGALA ROAD FROM 11+500 TO 17+000 KM'**, under Contract No: **RDA/RM&M/EP(Akk)/RMI/2024/13** for the Contract Price of Rupees as corrected in accordance with Instruction to Bidders is hereby accepted.

You are hereby instructed to proceed with the execution of the said Works in accordance with the Contract Documents.

The Commencement Date shall be

The amount of Performance Security is.....

The Performance Security shall be submitted on or before

Authorized Signature Name & title of Signatory Name of Agency

FORM OF PERFORMANCE SECURITY

(Unconditional)

[Issuing Agency's Name, and Address of Issuing Branch or Office]

Beneficiary: Director General, Road Development Authority (hereinafter called and referred to as "the Employer") 1st floor, "Maganeguma Mahamedura", 216, Denzil Kobekaduwa Mawatha, Battaramulla.

Date:

PERFORMANCE GUARANTEE No.:

(hereinafter called, "the Contractor") has entered into Contract No. RDA/RM&M/EP(Akk)/RMI/2024/13 dated with you, for the 'RECTIFICATION AND ASPHALT SURFACING ON AMPARA IGINIYAGALA ROAD FROM 11+500 TO 17+000 KM', (hereinafter called "the Contract").

Furthermore, we understand that, according to the Conditions of the Contract, a performance guarantee is required.

This guarantee shall expire, no later than the day of202.... [28 days beyond the Defect Notification Period] and any demand for payment under it must be received by us at this office on or before that date.

Name, Signature an	d the Seal of the Agency:		
Name of the Organi	zation		
Designation			
Date:			
Witness:			
Name	NIC No	Signature	
Name		Signature	

FORM OF AGREEMENT

Whereas the Employer desires that the Contractor execute "RECTIFICATION AND ASPHALT SURFACING ON AMPARA IGINIYAGALA ROAD FROM 11+500 TO 17+000 KM", under Contract No: RDA/RM&M/EP(Akk)/RMI/2024/13 (hereinafter called and referred to as "the Works") and the Employer has accepted the Bid by the Contractor for the execution and completion of such Works and remedying of any defects therein.

The Employer and the Contractor agree as follows:

CON

- 1. In this Agreement words and expressions shall have the same meanings as are respectively assigned to them in the Contract.
- 2. In consideration of the payments to be made by the Employer to the Contractor as indicated in this Agreement, the Contractor hereby covenants with the Employer to execute and complete the Works and remedy any defects therein in conformity in all respects with the provisions of the Contract.
- 3. The Employer hereby covenants to pay the Contractor in consideration of the execution and completion of the Works and remedying any defects therein, the Contract Price or such other sum as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract.

In Witness whereof the parties hereto have caused this Agreement to be executed on the day and year aforementioned in accordance with laws of Sri Lanka.

Name:	Authorized Signature of Employer Name & Title of Signatory
Authorised Signatory of Contractor	
In the presence of Witnesses:	In the presence of Witnesses:
1. Name	1. Name
NIC No	NIC No
Signature	Signature
Address	Address
2. Name	2. Name
NIC No	NIC No
Signature	Signature
Address	Address

FORM OF ADVANCE PAYMENT SECURITY

[Name and address of Agency, and Address of Issuing Branch or Office]

Beneficiary: Director General , Road Development Authority (hereinafter called and referred to as "the Employer") 1st floor, "Maganeguma Mahamedura", 216, Denzil Kobekaduwa Mawatha, Battaramulla.

Date:

ADVANCE PAYMENT GUARANTEE No.:....

The maximum amount of this guarantee shall be progressively reduced by the amount of the advance payment repaid by the Contractor.

This guarantee shall expire on[insert the date, 28 days beyond the Time for Completion]

Consequently, any demand for payment under this guarantee must be received by us at this office on or before that date.

Name, Signature and the Seal of	of the Agency:	
Designation		
Name of the Organization		
Date:		
Witness:		
Name	NIC No	Signature
Name	NIC No	Signature

FORM OF RETENTION MONEY GUARANTEE

(Issuing Agency's Name and Address of Issuing Branch or Office

Beneficiary: Director General, Road Development Authority, 1st Floor, Maganeguma Mahamedura",216, Denzil Kobekaduwa Mawatha, Battaramulla. Date: ------

RETENTION MONEY GUARANTEE No.:-----

We have been informed that ------(name of Contractor) (hereinafter called "the Contractor") had entered into Contract No: RDA/RM&M/EP(Akk)/RMI/2024/13 dated2024, with you, for the execution of 'RECTIFICATION AND ASPHALT SURFACING ON AMPARA IGINIYAGALA ROAD FROM 11+500 TO 17+000 KM'. (hereinafter called "the Contract")

Furthermore, we understand that, according to the Conditions of Contract, when the works have been taken over and the first half of the Retention Money has been certified for payment, payment of the second half of the Retention Money may be made against a Retention Money guarantee.

At the request of the Contractor, we ------(name of agency) hereby irrevocably undertake to pay you any sum or sums not exceeding in total an amount of ------ (amount in figures)--------(amount in words) upon receipt by us of your first demand in writing accompanied by a written statement stating that the Contractor is in breach of its obligation under the Contract because the Contractor has not attended to the defects in accordance with the Contract.

The guarantee shall expire, at the latest, ------ (insert 28 days after the end of the Defects Notification Period). Consequently, any demand for payment under this guarantee must be received by us at this office on or before that date.

Name, Signature and the Seal	of the Agency:	
Name of the Organization		
Designation		
Date:		
Witness:		
Name	NIC No	Signature
	NIC No	-



VOLUME 2

- Invitation For Bids
- Section 2 Bidding Data
- Section 4 Contract Data
- Section 6 Specifications
- Section 7 Form of Bid
- Section 8 Bill of Quantities
- Section 9 Schedules
- Section 11 Standard Forms (Bid)
- Section 10 Drawings

GOVERNMENT OF THE DEMOCRATIC SOCIALIST REPUBLIC OF SRI LANKA MINISTRY OF TRANSPORT & HIGHWAYS ROAD DEVELOPMENT AUTHORITY <u>INVITATION FOR BIDS</u>

1. The Chairman, Road Development Authority Procurement Committee, on behalf of the Road Development Authority (RDA), invites sealed bids from eligible and qualified bidders for the *project* described below:-

2.					
		Eng.'s Estimate	Contract	CIDA	Bid Security
Contract No	Contract Name	w/o	Duration	Grade	(Rs)
Contract No.	Contract No. Contract Name	contingencies	Days		
		(Mn)			
	Rectification and Asphalt Surfacing on	130.5	273	C3 or	2,280,000.00
RDA/RM&M/EP(A kk)/RMI/2024/13 kk)/RMI/2024/13				above in	
			Highway		
	10 17+000 km			speciality	

- 3. The work consists of rectification and asphalt surfacing on Ampara Iginiyagala Road From 11+500 to 17+000 km.
- 4. Bidding will be conducted through the National Competitive Bidding Procedure.
- 5. To be eligible for contract award, the successful bidder shall be currently registered with the Construction Industry Development Authority (CIDA) in grade given in the above table in Highway specialty.
- 6. Interested bidders may obtain further information from the following offices and inspect the bidding documents via website www.rda.gov.lk. From 26/06/2024
 - Additional Provincial Director (Akkaraipattu), Additional Provincial Director's Office, Road Development Authority, Akkaraipattu.
 T: 067-5577428 Fax: 067-2278971
 - Deputy Director General (RM & M), Road Development Authority, 6th Floor, "Maganeguma Mahamedura", 216, Denzil Kobekaduwa Mawatha, Battaramulla.
 T P :011-2882196 Fax: 011-2882195
- 7. The Pre-Bid meeting will be held at 10:00 hrs on 04/07/2024 at the office of the a. Additional Provincial Director (Akkaraipattu), Additional Provincial Director's Office, Road Development Authority, Akkaraipattu and a site visit will be arranged immediately thereafter if necessary.
- 8. A complete set of Bidding Document in English Language shall be purchase by the interested bidders via email on submission of a written application and valid cash deposit slip of non refundable tender fee (Contract number, contact number and company name of bidder should be indicated on the cash deposit slip) to Deputy Director General (Road Maintenance & Management), RDA via email from 26/06/2024 until 16/07/2024 during 09.00 hrs to 15.00 hrs.

The email address is mmtenders123@gmail.com

Non – refundable tender fee of Rs. 30,250.00 (with SSCL & VAT) for bidding document can be paid by depositing cash to the following bank account.

Account Name	:	Director General – RDA
Account Number	:	000001943
Bank Name	:	Bank of Ceylon – Corporate Branch

Original / valid cash deposit slips should be submitted with the Bids at the submission of bids and it will be checked.

As per the Public Contract Act No. 3 of 1987, only the Agents and Successful winners of tenders shall be registered in Department of Registrar of Companies.

- Each Bid shall be accompanied by a Bid- Security according to the format given in the bidding document for an amount given in the above table. The beneficiary of the bid security shall be Director General, Road Development Authority. Bid- Security shall be valid up to 13/11/2024. Bids shall be valid up to 16/10/2024.
- 10. Bid, with original cash deposit slip, shall be delivered in duplicate to the Chairman, Road Development Authority Procurement Committee, C/o Director General, Road Development Authority, First Floor, "Maganeguma Mahamedura", 216, Denzil Kobekaduwa Mawatha, Battaramulla on or before 14:00 hrs on 17/07/2024. Late bids will be rejected. Bids will be opened soon after the closing, in the presence of the bidder's representatives who choose to attend.

The Chairman, Road Development Authority Procurement Committee Road Development Authority, First Floor, "Maganeguma Mahamedura", 216, Denzil Kobekaduwa Mawatha, Battaramulla.

SECTION - 2

BIDDING DATA

This Section shall be read in conjunction with Section 1- 'Instruction to Bidders', and is intended to provide specific information in relation to corresponding clauses in Section 1. Wherever there is a discrepancy, the provisions of Section-2-.Bidding Data shall supersede those provided in the Section 1 – Instructions to Bidders.

The Clause numbers given in this Section correspond to the Clauses with the same numbers in the Section 1 -'Instruction to Bidders'.

Whenever a Clause number appears in this Section, it means the information in the corresponding Clause in Section 1 is supplemented and/or modified according to the information in the Clause in Section 2.

If a Clause number does not appear in this Section, it means the Clause with the corresponding number in Section 1, remains unchanged.

BIDDING DATA

Instructions to Bidders Clause Reference 1.1

Employer's Name and Address

Employer is the Road Development Authority established by the Road Development Authority Act No. 73 of 1981 as amended by Act No.05 of 1988 and No.37 of 2009.

Address of the Employer is

"Maganeguma Mahamedura" 216, Denzil Kobbekaduwa Mawatha, Battaramulla. Telephone: 0112862795 Fax: 0112872272

Scope of Works is rectification and asphalt surfacing on the on AMPARA IGINIYAGALA ROAD FROM 11+500 TO 17+000 KM.

The work consists of rectification and asphalt surfacing on Ampara Iginiyagala Road from 11+500 to 17+000 km.

1.2 Time for Completion

The Time for Completion of the whole of the Works shall be **273 Days** from the Commencement Date.

2.1 Source of funds

The source of funds is Government of Sri Lanka (RMI)

3 Add a new sub-Clause 3.3

Clause 3.3

A misrepresentation or omission of facts in order to influence the procurement process shall make the Bid non-responsive and if detected after the award the bidder could be subjected to legal prosecution.

4.1 Qualification Information

The following information shall be provided in Section – 9 – Schedules;

•	CIDA registration	
	Registration numb	er
	Grade	
	Specialty	
	Expiry date	

- If not VAT registered, self declaration on VAT registration
- VAT registration number
- If a Joint Venture, the agreement
- Construction Programme with critical path and cash flow forecast.
- Legal status of the bidder (sole proprietor, Partnership, Company etc.)
- Authentication signatory (written Power of Attorney, affidavit for signatory)
- Total monetary value of construction work performed for each of the last five years.
- Experience in works of a similar nature and size for each of the last ten years.
- Availability of Construction equipment.
- Availability of Staff
- Work plan and methods

- Information on current work in hand
- Certified copy of Audited Financial Report for last five years.
- Non Performing Contracts
- **4.2(a)** The bidders shall have a valid registration in Grade C3 or above, in Highway Specialty, on the date of closing of bids.
- **4.2(b)** Average annual volume of construction work performed during last five years shall be at least **Rs. 228.3 million.**

Annual Average Construction Turnover (AACT) is calculated as follows,

AACT = \sum ACTn where, n= 1st5th year (last five years) 5

ACTn - Annual Construction Turnover of nth year (from the audited financial report)

4.2(c) The Bidder should have at least one contract experience as prime contractor in construction or rectification of substructure of bridge of nature and complexity similar to the Works, the value of which should be at least **Rs. 106.5 million** during the last ten years. (to comply with this requirement, works cited should be at least 70 percent complete).

4.2(d) Essential equipment

Proposals for the timely acquisition (own, lease, hire, etc.) of the following essential equipment shall be ,

Machinery	<u>Capacity</u>
1. Motor Grader	100 HP or above
2. Excavator	0.5 Cum (3Nos)
3. Hand Rammer	operating wt. > 70kg
4. Vibrating Roller	2 Tons
5. Dump trucks	
6. Emulsion sprayer	
7. Backhoe Loader	0.5 m ³ Scoop capacity
8. Water Bowser	6000 Lit
9. Asphalt Pavers	10MT
10. Pneumatic tired roller	8 – 10 Ton
11. Air compressors	250 CFM

4.2 (e)

The Contract Manager shall have following qualification & experience,

Four Years B.Sc Engineering (Civil) Degree from a University in Sri Lanka or equivalent Civil Engineering Qualification recognized by the UGC and Institution of Engineering, Sri Lanka (IESL). OR Passed Part I, II and III examinations of the Institution of Engineers, Sri Lanka(IESL) OR B.Tech Degree in Civil Engineering from the Open University of Sri Lanka. The person shall have 5 years experience in the Highway Construction and shall have ability to lead and direct multi-disciplinary teams and experience in proper deployment and efficient management of human and other resources.

4.2 (f) Liquid assets and / or credit facilities required

The minimum amount of liquid assets available shall be Rupees 50.7 million.

The minimum amount of liquid assets available is calculated as follows.

$$X = (A - L) - 0.1 W + C$$

Where,

- X = Minimum amount of liquid assets available,
- A = Current assets as given in the latest audited financial statements,
- L = Current liabilities as given in the latest audited financial statements,
- W = Outstanding contractual commitments as supported by an affidavit as per Form No. 07,
- C = Project specific revolving line of credit given by a bank as per given Form

Note : Available Working Capital of bidder should be positive (+).

Add new clauses 4.2 (h) & 4.2 (i)

4.2 (h) Non - Performing Contracts

Criteria	Compliance Requirements				Documents
Requirement	Single Entity	All Partners Combine d	Joint Venture Each Partner	One Partner	Submission Requireme nts
Non- performance* in a contract has not been occurred as a result of Contractor's default	must meet requiremen t by itself or as partner of JV	not applicabl e	must meet requirement by itself or as partner of JV	not applicabl e	Schedule No. 09 (a) & 09 (b)

* All RDA projects (foreign & local funded) shall be considered for assessment of Non-performing Contracts (single entity contractor / any JV / any each partner of the JV, nominated sub-contractor) based on the following criteria.

1. Any bidder who submits bid to this contract shall be disqualified for the award of the contract, if Notice to Correct (NC) has been issued as per Clause 15.1 of SBD 2 Condition of Contracts on the poor performance of the Contractor or similar notice as per the relevant Conditions of Contract (COC) and is imposed before 28 days prior to date of bid opening (22/05/2024), unless the Engineer certifies that Contractor has corrected the contents of the Notice to Correct. This certificate shall be accompanied with the bid; or

If any Contract has been terminated due to the Contractor's default within last five years prior to June 19, 2024, he shall be disqualified for the award of contract.

4.2 (i) Pending Litigation and Arbitration

Criteria		Compliance	Requirements	5	Documents	
			Joint Venture			
Requirement	Single Entity	All Partners Combined	Each Partner	One Partner	n Requireme nts	
All pending	must	not	must meet	not	Schedule	
litigation and	meet	applicabl	requirement	applicabl	No. 10	
arbitration, if	requirem	e	by itself or	e		
any, shall be	ent by		as partner to			
treated as	itself or as		past or			
resolved	partner to		existing			
against the	past or		Joint			
Bidder and so	existing		Venture			
shall in total	Joint					
not represent	Venture					
more than fifty						
(50%) percent						
of the Bidder's						
net worth						
calculated as						
the difference						
between total						
assets and total						
liabilities.						

10.1 Clarification of Bidding Documents

Employer's address for clarification of bidding documents is.

Deputy Director General (RM & M),

RDA, 6th Floor, "Maganeguma Mahamedura", Denzil Kobbekaduwa Mawatha, Battaramulla

Phone: 011 – 2882196 Fax No. 011 – 2882195

14.3 Add following to this clause

All taxes except VAT shall be incorporated to the rates.

14.4 Adjustment for change in cost

The Contract is subjected to price adjustments.

Period of Bid validity:

The Bid shall be valid up to 16.10.2024.

17.1 Amount of Bid security:

The amount of Bid Security is Sri Lanka Rupees 2.28 Mn

17.2 Validity of Bid Security

The Bid Security shall be valid up to 13.11.2024. The form of Bid Security shall be strictly in the format given in the Bidding Document.

The Beneficiary of Bid Security shall be Director General, Road Development Authority. Any unconditional bank guarantee issued by an acceptable agency to the Employer is acceptable.

Any bond or security issued by ABC Insurance Company Limited is not acceptable.

18. Alternative Proposals by Bidders

Delete entire Clause and substitute with the following:-"Bidders are not allowed to submit alternate proposals"

19.1 Pre – Bid meeting

Pre-bid meeting will be held on 04.07.2024 at Additional Provincial Director (Akkaraipattu), Additional Provincial Director's Office, RDA, Akkaraipattu at 10:00 hrs. The site visit shall be arranged thereafter with RDA representative, if necessary.

20.4 Add new Sub Clause 20.4

All pages of the Bidding documents shall be signed by the bidder and his seal affixed.

21.2 Submission of Bid

21.2(a) Employer's address for the purpose of bid submission is ; Chairman, Road Development Authority Procurement Committee, C/o Director General, Road Development Authority, 1st floor, "Maganeguma Mahamedura" 216, Denzil Kobbekaduwa Mawatha, Battaramulla.

21.2(b) Name and Identification number of Contract The name of the Contract is RECTIFICATION AND ASPHALT SURFACING ON AMPARA IGINIYAGALA ROAD FROM 11+500 TO 17+000 KM, Contract Number is RDA/RM&M/EP(Akk)/RMI/2024/13.

22.1 Deadline for submission of Bids

The deadline for submission of bids is 14:00 hrs on 17.07.2024.

23.1 Any bid received after the deadline for submission of bid will be returned unopened to the bidder.

25.1 Bid Opening

35.1

The Bids shall be opened immediately after the deadline for submission of Bids, mentioned in sub-clause 21.2 & 22.1

Amount of Performance Security

The format of the security shall be strictly in accordance with the format given in Section 5.

The amount of Performance Security is 5% of the Initial Contract Price.

The Performance Security shall be valid until 28 Days beyond the defect notification period.

Any unconditional bank guarantee issued by registered bank in the Central bank of Sri Lanka or CGF is acceptable.

SECTION - 4

CONTRACT DATA

This Section shall be read in conjunction with Section 3- 'Conditions of Contract', and is intended to provide specific information in relation to corresponding clauses in Section 3. Wherever there is a discrepancy, the provisions in Section 4 – Contract Data shall supersede those provided in the Section 3 – Conditions of Contract.

The Clause numbers given in this Section correspond to the Clauses with the same numbers in the Section 3 – 'Conditions of Contract'.

Whenever a Clause number appears in this Section, it means the information in the corresponding Clause in Section 3 is supplemented and/or modified according to the information in the Clause in Section 4.

If a Clause number does not appear in this Section, it means the Clause with the corresponding number in Section 3, remains unchanged.

CONTRACT DATA

COC Clause Number/s					
1.1.2.2	Employer's Name :Road Development Authority established by the Act No 73 of 1981 as amended by Act No.05 of 1988 and No.37 of 2009.Employer's Address :"Maganeguna Mahamedura", 216, Denzil Kobbekaduwa Mawatha, Battaramulla				
1.1.2.4	The Engineer will be notified later.				
1.1.3.3	Time for Completion is 273 Days				
1.1.3.7	Replace with the following, The Defects Notification Period is one Year.				
1.3 (b)	Employer's Address "Maganeguma Mahamedura", 216, Denzil Kobbekaduwa Mawatha, Battaramulla. Engineer's Address : will be notified later				
2.1	The Start Date shall be 14 Days from the receipt of the Letter of Acceptance				
3.1	 The Start Date shall be 14 Days from the receipt of the Letter of Acceptance The Engineer shall obtain the specific approval of the Employer before taking action under the following Sub – Clauses of these Conditions. I. Clause 13.3 - Variation Procedure II. Clause 4.4 - Subcontractors III. Clause 5.0 - Nominated Subcontractors IV. Clause 8.4 - Extension of Time for Completion V. Clause 8.3.1 – Prolonged Suspension VII. Clause 11.3 – Extension of Defects Notification Period IX. Clause 11.3 - Extension of Defects Notification Period IX. Clause 11.6 - Adjustments in Changes in Legislation XI. Clause 16.4 - Payment on Termination Notwithstanding any obligations set out elsewhere in this Contract to obtain approval from the Employer, if, in the opinion of the Engineer, an emergency occurs affecting the safety of life or of the Works or of adjoining property, he may, without relieving the Contractor of any of his duties or responsibilities under the Contract, instruct the Contractor of shall such work or to do such things as may, in the opinion of the Engineer, be necessary to abate or reduce the risk. The Contract Price, in respect of such instruction, in accordance with Clause 13 and shall notify the Contractor accordingly, with a copy to the Employer. 				

4.2	Performance Security					
	Amount of Performance Security is 5% of the Initial Contract Price. The acceptable format of the Performance Security is given in this Bidding Document.					
	Any unconditional bank guarantee issued by registered bank in the Central bank of Sr Lanka or CGF is acceptable.					
	Change the Heading from 'Quality Assurance' to 'Quality Control'					
4.17	Replace the text of the Sub-Clause 4.17 with the following text:					
	4.17(a) Identifying Defects The Engineer shall check the Contractor's work and notify the Contractor of any Defects that are found and shall specify a time within which the defects are to be rectified. Such checking shall not affect the Contractor's responsibilities. The Engineer may instruct the Contractor to search for a Defect and to uncover and test any work that the Engineer considers may have a Defect.					
	4.17(b) Tests If the Engineer instructs the Contractor to carry out a test which is not specified in the Specification or Bills of Quantities in sufficient details to enable the Contractor to have priced or allowed for the same in the Bid and the test shows that the workmanship or Material is defective then the Contractor shall pay for the tests and samples.					
	If the test shows that the workmanship and Materials is in accordance with the Contract and if the Contractor suffers delay and /or incurs Cost from complying with these instructions or as a result of delay for which the Employer is responsible, the Contractor shall give notice to the Engineer and shall be entitled subject to Sub-Clause 19 (Contractor's Claims) to: (a) an extension of time for any such delay, if completion is or will be delayed, under Sub-Clause 8.4 (Extension of Time for Completion): and					
	 (b) payment of any such Cost plus reasonable profit, which shall be included in the Contract Price. After receiving this notice, the Engineer shall proceed in accordance with Sub- 					
	Clause 3.4 (Determinations) to agree or determine these matters. The Contractor shall promptly forward to the Engineer duly certified reports of the tests. When the specified tests have been passed, the Engineer shall endorse the Contractor's test certificate, or issue a certificate to him, to that effect. If the Engineer has not attended the tests, he shall be deemed to have accepted the readings as accurate.					
	4.17(c) Correction of Defects					
<i>y</i>	4.17(c-1) The Engineer shall give notice to the Contractor of any Defects before the end of the Defects Notification Period, which begins at completion, and is defined in the Contract Data.					
	4.17(c-2) Every time notice of a Defect is given, the Contractor shall correct the notified Defect within the length of time specified by the Engineer's notice.					

	4.17(c-3)				
	4.17(C-3) On completion of the Defects Notification Period and correction of Defe accordance with Sub-Clause 4.17(c-2) or 4.17(d), and on certification of final payment, the Engineer shall issue the Final Payment Certificate to t Contractor				
	4.17(d)	Uncorrected Defects If the Contractor has not corrected a Defect within the time specified in the Engineer's notice, the Engineer will assess the cost of having the Defect corrected, and the Contractor will pay this amount.			
8.7		Liquidated Damages			
		The Liquidated Damages for the whole of the works shall be Rs. 76,093.00 per Day.			
		The maximum amount of Liquidated Damages for the whole of the works shall be 10% (ten percent) of the Initial Contract Price.			
12.2(b)		he method of Measurement shall be as per the Contract			

13.3	Variation Procedure				
	Replaced with				
	 Variation Exceeding 25 percent If on the issue of the Taking Over Certificate for the whole of the Works it is found that there is a reduction or increase of more than 25% in the Quantity of any unit priced items in the original Bill of Quantities for which the total cost based on the rate for that item in the Bill of Quantities is more than 5% of the "effective Contract Price" (which for the purpose of this sub- clause shall be the contract price, excluding the provisional sums and allowances for day works, if any, and the adjustment of price under sub clauses 13.6 and 13.7 at statement at completion) then, a. The excess quantity of particular item shall be paid as describes in following table 				
	a.		rticular item shall be paid as describes	s in following table	
		Excess quantity	Method of payment		
		up to 25%	Original Bill of Quantity rate		
		Between more than	90% of Original Bill of Quantity		
		25% and less than 50%	rate		
		more than 50%	83% of Original Bill of Quantity		
rate					
	 b. Quantity reduction of particular item shall be paid as described below If the final quantity of work done in particular item is 75% of the original Bill of Quantities or less shall be paid at the rate shown in the Bill of Quantities. In addition a payment of 17% of the difference between 75% of the estimated amount for that item and the final amount for that item shall be made to the Contractor. 				
		• 7,7			

13.4(b)	Percentage for adjustment of Provisional Sums				
	 For the works executed by Utility Authorities - 10% For the works directly executed by the Contractor – 20% For supplying and services-10% 				

13.7	Price Adjustment The Contract is subjected to price adjustment					
		M30B	Bitumer	1	54.57	
		P1		luipment	12.12	
		Р3	Fuel		8.69	
		M45	Metal		8.13	
		M55	Earth		2.30	
		P2	Heavy E	quipment	1.85	
		L3	Unskille	d Labour	1.31	
		L2	Semi ski	lled Labour	0.72	
		L1	Skilled L	abour	0.31	
			Total		90.00	
	-	Non - adjustable items shall be bill no. 01 (Preliminaries & Generals), bill no. 06 (Dav Norks) and all PS & LS items.				s), bill no. 06 (Day
	Advance Payment A total Advance Payment of 20% of the Initial Contract Price net of Contingencies and Provisional Sums would be made in two equal instalments on submission of an advance payment guarantee. The second instalment would be paid only after establishing that the first instalment of the advance payment has been used exclusively for mobilization of this project and submission and approval of detailed construction programme with network analysis and resource scheduling. The advance payment guarantee shall only be from a Bank registered in the Central Bank of Sri Lanka or CGF. First part of the advance payment would only be paid after signing of a formal contract agreement .					
14.3(c)	Percentage of retention			10%		
	Limit of Retention Money		5% of the Initial Contract Price			
14.5	Minimum amount of Interim Payment Certificates		8,485,000.00 Million Rupees. (Rupees Eight Million Four Hundred and Eighty Five Thousand).			
15.2 (h)	Add followi	-				
	Termination by Employer If the delay is more than the period, for which the Maximum Delay Damage is allowed to be applied, the Employer may consider this situation as Contractor's fundamental breach of the Contract, and the Employer may consider Termination of the Contract. The Delay is determined by updating the approved program with actual progress, after saving the approved program as a Baseline.					
18.2	Third Party I	nsurance		This amount of is Rupees 5,00	of third party insura 10,000.00	nce per occurrence

SECTION - 6

SPECIFICATIONS

SPECIFICATION

Standard Specifications

The Standard Specifications comprise 'Standard Specifications for Construction and Maintenance of Roads and Bridges' issued under the authority of the Director General of the Road Development Authority and published by the Institute of Construction Training and Development. The ICTAD Publication No. of this publication is SCA/5 Second Edition –June 2009

Bidders who are not in possession of this publication can purchase it from the CIDA.

PARTICULAR SPECIFICATIONS

PREAMBLE

These Particular Specifications should be read in conjunction with the Standard Specifications for Construction and Maintenance of Roads and Bridges, ICTAD Publication No SCA/5Second Edition –June 2009, which are applicable in all cases not covered herein.

The Particular Specifications for some sections of the works are comprehensive and cover the full extent of the works in these sections. In other sections they apply in conjunction with the Standard Specifications. Finally in some sections not covered in the Particular Specifications, the Standard Specifications shall apply in full.

Where there is an ambiguity or discrepancy between the Particular Specifications and the Standard Specifications, the Particular Specifications shall prevail.

PRELIMINARIES & GENERAL

P001. MOBILIZATION AND DEMOBILIZATION

The Contractor shall submit to the Engineer within 14 days from the date of Letter of Acceptance his mobilization and demobilization plan for equipment, plant and machinery required for the Project. Plan shall include the location of plant, machinery and equipment and mode of transport. Engineer shall approve the mobilization and demobilization plan and payment shall be based on schedule of mobilization.

<u>Payment</u>

Payment shall be made according to the schedule submitted by bidder and within the lump sum amount agreed in the Bill of Quantities.

Item No P (001)	Description Mobilization & De-Mobilization of Contractor's facilities and Plant / Equipment	Pay Unit L.S.

120 AS BUILT DRAWINGS

120.1 Description

The work shall consists of preparation of As Built Drawings necessary for performance of the completion of the work covered by the Contract, the Contractor shall supply them by the dates stated in the Contract Data.

The Contractor shall retain, at his sole expense, a qualified engineer for appropriate on site construction inspections to ensure that all improvements as set forth required, pursuant to RDA standards and specification, and as-built shall be provided. The contractor shall certify, in writing, to the Engineer that the improvements were done in compliance with the approved plan or agreement pursuant to RDA Standards & Specifications and as-built shall be provided.

Field managed record drawings should be provided to the Engineer with indicating additions and deletions for approval before preparation of the final as-built Drawings.

The following requirements shall be applied to each as-built drawing developed for the project and a hard copy together with an electronic CAD drawing file in digital format on CD shall submit for the Engineer.

120.2 Construction Requirement

The following items shall be required for all "As-Built Drawings.

- (a) All as-built for projects are required to be on A1 or similar size of construction drawings and shall bear the name and address, of the person who preparing the drawings and the date the as-built data is added to the original via the revision block. Electronic Auto CAD drawing files, based on the GPS coordinate, are also required (if the construction drawings are prepared based on GPS coordinates). Surveyor's/Engineer's statement (with embossed or wet seal and with an original signature on each sheet) shall verify that as-built drawings reflect the true conditions in the field.
- (b) Contractor's statement (with an original signature on each sheet) shall verify that all construction specifications and product qualities have been met or exceeded.
- (c) "AS BUILT DRAWINGS" of "RECORD DRAWING" shall be clearly labelled on each sheet.
- (d) If the details of under-ground service lines (Water, Sewerage, ducts &etc) are available needs to be included to the as-built drawings on the approval of Engineer
- (e) The location and elevation of the benchmark referenced will be shown on the drawing. If the reference benchmark is within the project, then a complete description of its location will be provided to assist in future locating.

- (f) Survey data, relative to the GPS coordinate grid, on right-of-way monuments installed or encountered within the project
- (g) Note any changes to the alignment either vertically or horizontally of curb & gutter sidewalk, pavers or any other surface improvement.

120.3 Measurement & Payments

No payment shall pay for the preparation of As built drawings. If the Contractor does not supply the As Built Drawings by the dates stated in the contract data, or they do not receive the Engineer's approval, the Engineer shall withhold the release of Final payment of the Contract.

1.01 LAND AVAILABLE

The land available to the Contractor free of charge shall be the land occupied by the permanent works or the existing road right of way, whichever is greater in width.

1.02 DAMAGE TO LAND AND CROPS

Where land is made available to the Contractor free of charge, the Contractor shall under no circumstances interfere with this land whether for Permanent or Temporary works until the evaluation of all compensation has taken place and permission to proceed has been received from the Engineer.

Care shall be taken during the Works to ensure that no unnecessary damage is caused to the land or crops and that all reasonable precautions are taken to prevent soil erosion and mosquito breeding. On completion of the work, the land shall be left in a tidy condition as directed by the Engineer.

1.03 **GRAVES, TOMBS, RELIGIOUS OR TRADITIONAL MONUMENTS**

Areas which contain graves, tombs and religious or traditional monuments within the Site shall be cleared by the Contractor in accordance with the written instructions of the Engineer.

1.04 CONTRACTOR'S HOUSING, STORES AND WORKSHOP AREAS

The location and layout of housing, stores and workshop areas together with their use and detailed dimensions shall be approved by the Engineer. The Contractor shall not erect any structures on the Site without the approval of the Engineer.

On the commencement of the Contract the Contractor shall fence off all areas designated for housing, plant-yard, workshops, offices and the like. By the end of the Period of Defects Notification Period or at such earlier time as the Engineer may instruct or approve, the Contractor shall clear all structures, plant and rubble from these areas and leave them in a condition acceptable to the Engineer.

1.05 FIRST AID FACILITIES

The first aid, welfare and safety standards to be provided and observed shall be at least equal to those laid down by the Ministry of Health/Labour for Industrial sites of similar size and remoteness and approved by the Engineer.

The Contractor shall, within 24 hours of the occurrence of any accident at or about the Site or in connection with the execution of the Works, report such accident to the Engineer and to the Competent Authority where required by Law. At least one person permanently on the Site shall have been trained in first aid and the person so designated shall have been made known to the Engineer in writing and to all employees by the posting of his name and designation in a prominent position on the Site.

1.06 SECURITY SERVICES FOR ENGINEER

The Contractor shall be responsible for all matters of security concerning the vehicles and housing, offices for the Engineer. The costs in connection with this clause shall be deemed to be included in the Contractor's tendered rates.

1.07 WATER SUPPLY

The Contractor shall make his own arrangements and at his own costs for the provision from approved sources of adequate clear water for use in construction of the Works or otherwise. Quantities of water withdrawn from the approved sources shall be such that the requirements of the local population in respect of water for irrigation, drinking purposes, etc., are not interfered with. The Contractor shall have obtained permission from the appropriate Authorities in each case for the abstraction of water from any natural source, before the Engineer approves the use of such source.

1.08 SERVICES

The Contractor shall make his own arrangements for the supply of electricity for power and light and of any other services required in order to carry out the Works and he shall make his own arrangements, subject to the approval of the Engineer, for the disposal of sewage and all waste materials during the execution of the Works. All such services shall be at the Contractor's own expense.

1.09 **PROTECTION OF MAINS AND SERVICES**

The Contractor shall protect and support at his own costs during the construction of the Works, all pipes, mains, cables, overhead lines and other apparatus, which might be endangered by his operations.

In the event of any pipes, mains or cables being exposed at any time, the Contractor shall immediately notify the Authority or proprietor concerned and shall not cover the exposed pipe, main or cable until it has been examined and approved by the appropriate Authority or proprietor.

Before commencing any section of the Works the Contractor shall at his own expense obtain full information with regard to the position and depth of all pipes, mains and cables.

The Contractor is responsible for making arrangements with the Public Authorities and other duly constituted bodies for the phasing into his programme of works, of all the work which needs to be done by them or their contractors concurrently with the Works. If in the execution of the Works, any damage to any service or apparatus or any interruption of or delay to the provision of any service is caused, the Contractor shall bear and pay the cost reasonably incurred by the Authority or body concerned in making good such damage and shall make full compensation to the Authority or other body for any loss sustained by reason of such interruption or delay.

In the case of damage caused to water mains, pipes or fittings less than 2 inches in diameter the Contractor shall repair the damage himself at his own expense without delay. The Contractor shall be responsible for any damage caused to the permanent works or to adjacent property by water flooding due to damage caused by him to water mains, pipes or fittings.

1.10 QUARRIES AND BORROW PITS

The Contractor shall be responsible for opening up any quarry or borrow pit and shall organize his methods of operation so that only material of a type and quality approved by the Engineer shall be selected for use in the Works. The Contractor shall provide, erect, operate and maintain all plant necessary for their proper operation, together with any access roads, temporary bridges or the like necessary for the supply to the Works of the aforementioned and pay all charges incurred, including the rights for entering the land and extracting the material, or for any other compensation.

No claim shall be allowed for delays or for any other reason in this respect.

1.11 OTHER WORKS

During the course of the Contract the Employer may cause other works such as the installation or removal or resetting of services to be carried out, on through or adjacent to the Site.

The Contractor shall at all times comply with the requirements of the relevant Clauses of the Conditions of Contract in respect of these and any other Works not included in the Contract and shall allow reasonable access as approved by the Engineer on and through the Site of the Works to any other contractor or workmen who may be working on or near the Site for this reason at no extra cost.

1.12 **POSSESSION OF THE SITE**

Possession of the site will be in accordance with the General Conditions of Contract. Possession will be granted in accordance with the Contractor's Programme referred to in the Conditions of Contract and the Specifications and approved by the Engineer.

1.13 **BOREHOLE INFORMATION**

Information regarding the position and depth of boreholes and the results obtained are shown on the drawings and Contractor shall be deemed to have considered this information and checked its accuracy during the Tender Period, and to have satisfied himself of the characteristics of the materials and the suitability of the plant and the methods of working on which he has based his rates.

1.14 WEATHER CONDITIONS

The Contractor shall not be entitled to extra payment by reason of the occurrence or effect of high winds, excessive rainfall, temperature, humidity or any other meteorological phenomena.

1.15 **PROGRAMME**

In addition to the requirements of the Conditions of Contract the Contractor shall furnish to the Engineer within one calendar month from the commencement date a detailed programme of the order in which he proposes to carry out the Works. The programme shall include time and progress charts so that actual progress on each operation can be shown against anticipated progress. Due allowance should be made for the seasonal rains and also in accordance with the relevant clauses in this specifications.

The Contractor shall keep the progress of the Works under continuous review. When necessary the programme shall be updated at regular intervals as required by the Engineer.

1.16 CONTRACT DOCUMENTS AND DRAWINGS

The Contractor shall be issued Contract Documents and Drawings. When necessary the Contractor shall also be supplied with two copies of any further drawings, which may be issued in accordance with the Contract.

1.17 **PRESERVATION OF SURVEY MARKERS**

The Contractor shall locate and where possible preserve or else relocate all survey markers established for the execution of the Works. Where such survey markers will be disturbed, the Contractor shall accurately reference these to permanent concrete markers before such work is commenced.

Where it is likely that any survey marker which is the property of the Survey Department will be disturbed, the Contractor shall inform the appropriate Survey Authorities at least 14 days before the marker is endangered and ensure that the Survey Authorities take appropriate action.

1.18 **DIMENSIONS AND LEVELS**

The Contractor on the Site shall verify all Dimensions and levels shown on the Drawings or mentioned in documents forming part of or issued under the Contract and he shall immediately inform the Engineer of any apparent errors or discrepancies in such dimensions or levels.

1.19 **NIGHT WORKING**

The Contractor may be permitted to carry out work during the night and shall submit full details of the methods of working and lighting, control of traffic and any other information, which the Engineer may request. No night working shall be carried out without the Engineer's approval, and the Engineer has the right to withhold or withdraw approval if, in his opinion, such work presents undue hazard or disturbance to the public, or is in any other way unsatisfactory.

The Contractor's intentions on night working shall be made known to the Employer on the programme of Works supplied with his tender.

1.20 AMENITY AND ACCESS

The Contractor shall ensure that, in carrying out the Works, he causes no damage by plant, workmen, flooding, subsidence or otherwise to any property. He shall take all precautions to the satisfaction of the Engineer to ensure that such hazards are avoided and public amenity maintained, and he shall be responsible for any damage that may occur.

The Contractor shall be responsible for providing and maintaining access to and along the Site for his own purposes, including any temporary river or swamp crossings he may require.

1.21 WORKS DURING DEFECTS NOTIFICATION PERIOD

After the Commencement of the Defects Notification Period, which shall normally, the Contractor shall do nothing which might endanger the safety of the public and he shall complete any outstanding works and undertake the correction of all defects as instructed by the Engineer or any other duly authorized person or Authority.

Throughout the Defects Notification Period the Contractor shall notify the Engineer of the work or operations he intends to carry out and he shall obey any instructions which the Engineer may give as to the times and manner of working so that any inconvenience to the public is kept to a minimum.

1.22 CLEARING AND TRIMMING OF SITE ON COMPLETION

On completion of the Works the Contractor shall leave the Site in a tidy condition to the satisfaction of the Engineer. Particular attention shall be paid to the final levelling, grading, making good of erosion gulleys and routings, landscaping and drainage of the Site, the borrow areas and any other places adjacent to the Site interfered with by the Contractor during the Construction or the Defects Notification Period.

1.23 SPILLAGES

The Contractor shall be responsible throughout the Contract and Defects Notification Period for any spillage of fuels, bitumen, hydraulics, oils, and other lubricants or materials caused by his activities on the Works and any such spillage shall be removed and any damage repaired to the satisfaction of the Engineer at the Contractor's expense.

1.24 APPROVAL OF SUPPLIERS OF MATERIALS AND GOODS

Before entering into any agreement for the supply of any materials or goods, the Contractor shall obtain the Engineer's approval in writing of the supplier from whom he proposes to obtain such materials or goods. Should the Engineer at any time be dissatisfied with such materials or goods or with the method or operations carried out by such sub-contractor's work or place of business, the Engineer shall be empowered to cancel his previously given approval of such sub-contractor/supplier. The Contractor shall then obtain such said materials or goods from other supplier as may be approved by the Engineer and shall bear any additional cost thereof.

1.25 COPIES OF ORDERS

The Contractor and sub-contractors shall provide the Engineer with copies of all orders, which they may place for the supply of materials or goods required in connection with the Works.

1.26 SAMPLES

In addition to any special provisions herein for the sampling and testing of materials, the Contractor shall submit to the Engineer as he may require, samples of all materials and goods, which he proposes to use or employ in or for the Works. Such samples, if approved, will be retained by the Engineer, and no materials or goods of which samples have been submitted shall be used on the Permanent Works unless and until such samples have been approved in writing by the Engineer. Notwithstanding the Engineer's approval as provided for herein the Contractor shall be solely responsible for the quality of all materials and goods supplied.

The cost of supplying all such samples and of conveying the same to such place of inspection or testing as the Engineer may designate within the country of origin and of complying with the requirements of this clause shall be deemed to be included in the rates and prices in the Contract.

1.27 **TEST CERTIFICATES**

Should the Engineer so require, the Contractor shall obtain Certificates of Tests from the suppliers of any Goods and shall send such Certificates to the Engineer. Such Certificates shall certify that the Goods concerned have been tested in accordance with the requirements of the Specification and shall give the results of all the tests carried out. The

Contractor shall provide adequate means of identifying the Goods delivered to the Site with the corresponding Certificates.


The test certificates shall not release the Contractor of any of his obligations under the Contract in connection with the specifications of the relevant Goods when incorporated to the Permanent Works, nor of the necessity for further testing as required in the Specifications or directed by the Engineer.

1.28 WORKS TO BE IN THE DRY

Unless otherwise specified all the works are to be carried out in the dry and they shall be kept free from water coming from whatsoever source to the satisfaction of the Engineer.

1.29 PAYMENT FOR COMPLYING WITH ITEMS 1.01 TO 1.28

There will be no separate payment for complying with the Items 1.01 to 1.28 of this section, and the cost of complying with all the requirements stated herein shall be deemed to be included in the Contractor's rates in the remainder Bills of the Bills of Quantities.

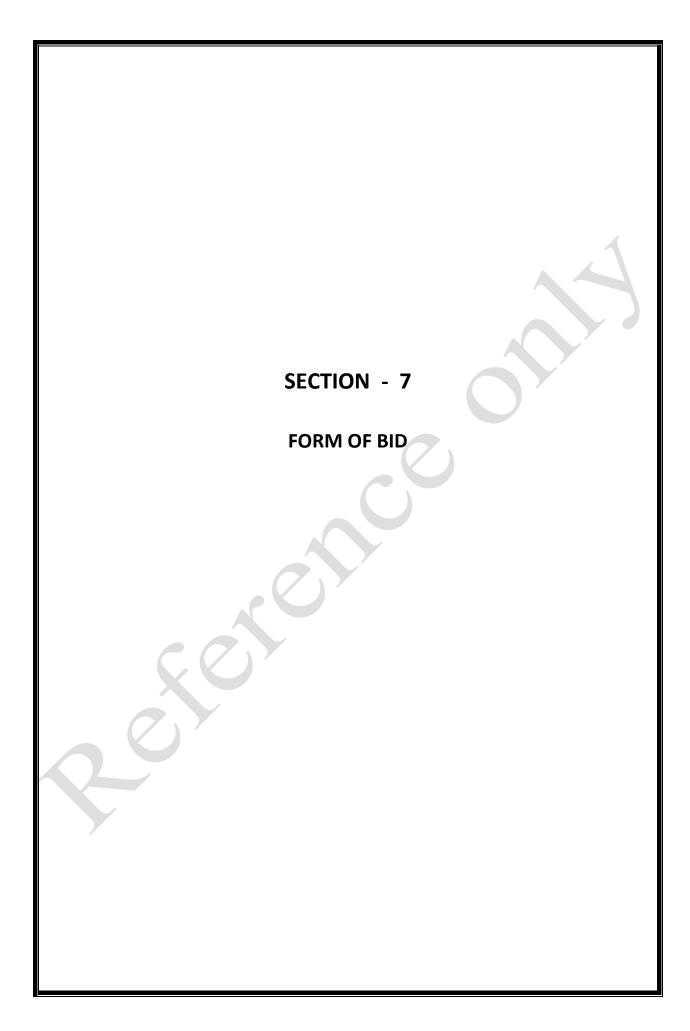

FORM OF BID

RECTIFICATION AND ASPHALT SURFACING ON AMPARA IGINIYAGALA ROAD FROM 11+500 TO 17+000 KM under Contract No: RDA/RM&M/EP(Akk)/RMI/2024/13

To: Road Development Authority.

Gentlemen:


- 2. We acknowledge that the Contract Data forms part of our Bid.
- 3. We undertake, if our Bid is accepted, to commence the Works as soon as is reasonably possible after the receipt of the Engineer's notice to commence, and to complete the whole of the Works comprised in the Contract within the time stated in the Contract data.
- 4. We agree to abide by this Bid until the date specified in ITB Clause 16..... and it shall remain bidding upon us and may be accepted at any time before that date.
- 5. Unless and until a formal Agreement is prepared and executed this Bid, together with your written acceptance thereof, shall constitute a binding Contract between us.[#]
- 6. We understand that you are not bound to accept the lowest or any bid you may receive.
- 7. We certify / confirm that we comply with the eligibility requirements as per ITB Clause 3 of the bidding documents.

Dated	this		da	y of			2024	in	the	capacity	of
			Duly aut		C	for and on beh	alf of				
Signatur	e		· · · · · · · · · · · · · · · · · · ·								
Witness	5	:	1 Name 2 Name			•					

* The amount inserted here should not include the VAT component

[#] For the joint venture bid, add following to item 5.0:

if this bid is a joint venture bid we undertake the responsibility to enter into a joint venture agreement among the joint venture partners. We are also well aware that in the event we fail to enter into a joint venture agreement the contract formed between us is null and void and our bid bond will be forfeited by you.

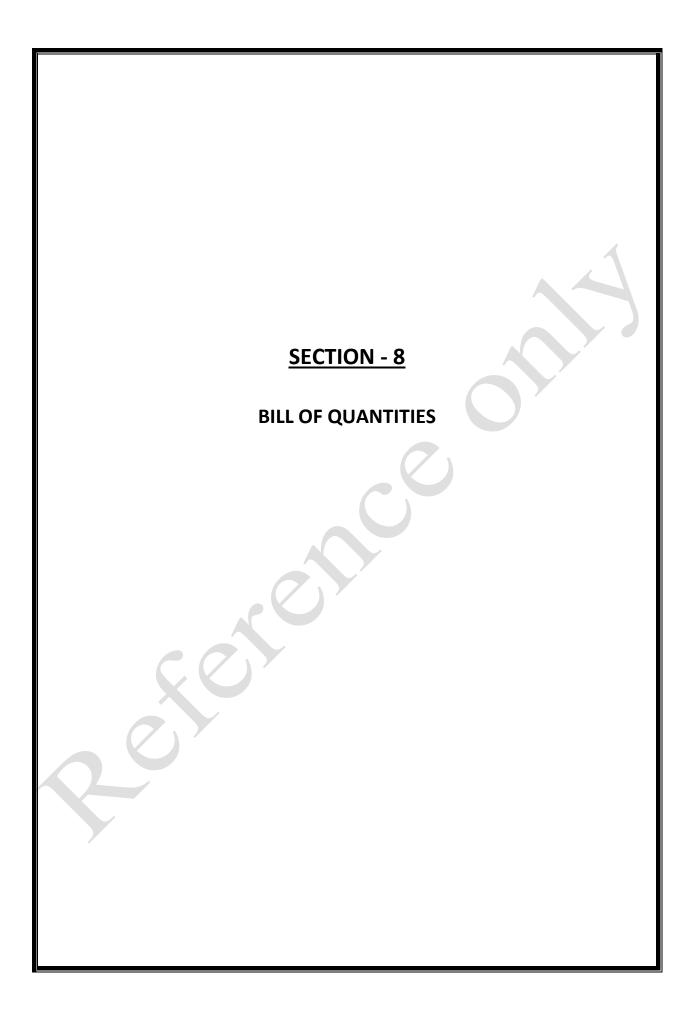

BILL OF QUANTITIES PREAMBLE

- 1. The Bill of Quantities shall be read in conjunction with all other sections of the bidding documents.
- 2. General directions and descriptions of work or materials given elsewhere in the bidding Documents are not necessarily repeated in the Bills of Quantities. For the full meaning of each Item, reference should be made to the applicable passages in the bidding documents.
- 3. The prices and rates entered by the contractor in the Bill of Quantities shall be deemed to cover the complete and finished works in the final position as required in the bidding documents, including, inter alia, all costs and expenses which may be required in and for the construction and maintenance of the works, together with all risks, liabilities, contingencies, insurance, sampling, testing, providing all necessary assistance to the Engineer and in general all obligations imposed or implied by the contract.
- 4. Without affecting the generality of the foregoing provisions the prices and rates entered by the contractor in the Bills of Quantities shall also include, inter alia, all costs and expenses involved with or arising from the following:
 - i. The provision, storage, transport, handling, use, distribution and maintenance of all materials, plant, equipment, machinery and tools, including all costs, charges, dues demurrage or other outlays involved in carriage and importation.
 - ii. The provision and maintenance of all staff and labour and their payment, accommodation, transport, fares and other requirements.
 - iii. Setting out, including the location, construction and preservation of survey markers, measurement and supervision.
 - iv. The provision, storage, transport, use, handling, distribution and maintenance of all consumable stores fuel, water and electricity including the requirements of the Engineer's Representative and his staff.
 - v. The location, test proving, opening, operation, reinstatement of al quarries and borrow pits, as well as compensation and mining royalties costs associated with quarries and borrow pits or any other land the contractor may require additional to that provided free for the execution of the permanent works.
 - vi. Sampling, the transport of samples, testing, the carrying out of trial sections of earthworks, or payment and the checking of all information given by the Engineer.
 - vii. Injury caused to the Works under Construction, Plant, Materials and consumable stores by weather.
 - viii. Repairs to the Works either prior to or during the Period of maintenance.
 - ix. Maintenance work as detailed in the Specifications and the Conditions of Contract and the maintenance of public amenities.
 - x. Co-ordination with other Contractors or Authorities carrying out work either in connection with or adjacent to the Works.
 - xi. The supply of manufactures test certificates

- xii. The protection of mains and services, and cost of repairs in case of damage caused by the Contractor.
- xiii. Pumping and de-watering; the protection of excavation faces.
- xiv. The provision and maintenance of temporary divisions in order that through traffic flow shall remain unobstructed through the contract period and in general the provision of all temporary works required in connection with the works.
- xv. Insurance, custom duties, taxes (without VAT), levies, first aid, welfare and safety requirements and all other overheads and costs, protection of existing bridge in case of stage construction and profit.
- 5. A price or rate shall be entered against each Item in the Bills of Quantities whether quantities are stated or not. Item against which no price or rate is entered shall be deemed to be covered by the other prices or rates entered by the Contractor in the Bills of Quantities. The unit price or rate entered against any Item shall take precedence over any miscalculation in the total sum against that Item. Where separate items have not been provided in the Bills of Quantities for work shall be deemed to have been included in the other prices and rates.
- 6. The Quantities given in the Bills of quantities are estimated only and are given to provide a basis for the tender. No guarantee is given for their accuracy and payments to Contractor will be based on the prices and rates quoted in the bills applied to measured quantities for work done.
- 7. The items in the Bills of Quantities are the general application to the whole of the works at any location on site or any part of the works as indicated in the bid documents or instructed by the Engineer's representative.
- 8. Tenders which group several items together in the Bill of Quantities under one price will not be accepted.
- 9. Item mentioned "Provisional" in the Bill of Quantities are not to be executed unless ordered by the Engineer. They may be expended wholly or in part or not at all as directed by the Engineer.
- 10. The Units of measurement described in the Bills of Quantities are Metric Units. Abbreviations in the Bill of Quantities are as follows:

		-	Hours	cu.deci.m	-	Cubic Decimeter
		-	Kilometre	km-mth	-	KilometreMonths
		-	Linear Metre	mnth	-	Month
		-	Square Metre	ltr	-	Litre
or cu	m	-	Cubic Metre	kg	-	Kilograms
		-	Numbers	MT	-	Metric Tonne
		-	Lump Sum	Veh-wk	-	Vehicle Week
		-	Provisional Sum			
or sqi or cui		-	Square Metre Cubic Metre Numbers Lump Sum	ltr kg MT	- - -	

DAY WORKS

- 1. The rates entered in the Schedule for Bill of Quantities shall form day works items for pricing extra work ordered to be done in accordance with the Contract.
- 2. The rates shall include all overheads and profit and all other costs of whatever nature necessary for and incidental to the performance of extra work whenever ordered and these rates required anywhere on the Site for the operation of plant the provision of labour or the provision of materials and shall be deemed to include inter alia:
 - Plant Operation, maintenance, repairs, fuel, oils grease, hydraulic fluids, taxes, duties operator's wages and overtime, travelling time, transport supervision, administration costs related to the use of such plant.
 - Labour Wages, overtime, bonuses, travelling time, hand tools, accommodation, fringe benefits, transport and supervision.

Materials Provision, transport, handling, wastage and storage.

In the case of Plant and labour, only time spent working shall be paid for.

For Day works required outside the <u>Site area</u> (which for these purposes shall mean all areas shown on the plans for permanent works and all areas of temporary works such as Contractor's and Engineer's camps, quarry, borrow pits and their access roads, diversion roads etc.), the following should be chargeable :

- Plant : Actual travel time from original work site to the place of day of work (without labour charge).
- Transport : Travelling time of the places of transport (lorry, low loader etc.)

Labour : Travel time for the means of transport used.

Materials : Travelling time for the means of transport used.

The rates shall apply only to such work, as the Engineer shall instruct in writing to be carried out as day works. All items should be priced.

Summary of Bill of Quantity

RECTIFICATION AND ASPHALT SURFACING ON AMPARA IGINIYAGALA ROAD FROM 11+500 TO 17+000 KM CONTRACT NO RDA/RM&M/EP(Akk)/RMI/2024/13

Bill No	Description	Description				
1	Preliminaries	& General				
2	Earth Works	Earth Works				
3	Sub Base, Bas	Sub Base, Bases and Shoulders				
4	Surface Applic	Surface Application and Surfacing				
5	Incidental Wo	rks				
6	Schedule of D	ay Works Rates				
Α	Sub Total-01					
В	Provisional su	Provisional sums (PS)				
С		Sub Total -02 without PS (A-B) (deduct PS from sub total 01)				
		Amount in words				
D	Discount if any		Amount in figures			
Ε	Sub Total 03 (C -D)				
F		Sub Total 04 with PS (E+B) (add PS to sub total 03)				
G	Allow for phys	Allow for physical contingencies 10% (F*10%)				
Н	Allow for price	Allow for price contingencies 7% (F*7%)				
Ι	Bid Price (F+C	Bid Price (F+G+H) [Form of Bid price]				
J	VAT (18%*I)					
К	Bid Price wit	Bid Price with VAT (I+J)				

Amount in words:

Name of Authorized Officer: _____

Signature: _____

RECTIFICATION AND ASPHALT SURFACING ON AMPARA-IGNIYAGALA ROAD (11+500-17+000) KM

Equipment Equipment SETTING OUT,CROSS SECTION SURVEYS AND DRAWINGS SETTING OUT,CROSS 1.3 SECTION SURVEYS AND DRAWINGS Image: Comparison of the comparison of th				-				
Bill Pay n n n n BILL No.1: PRELIMINARY GENERAL 1.1 TRAFFIC SAFETY & CONTROL 1.1 103(1) Management, Safety and Control and Temporary Diversion of Traffic, including provision of a general traffic management plan month 9 1.2 MOBILIZATION AND DEMOBILIZATION AND DEMOBILIZATION month 9 1.2.1 P(001) Contractor's facilities and Plant / Equipment LS SECTION SURVEYS AND DRAWINGS LS SECTION SURVEYS AND DRAWINGS 1.3.1 117(1) Longitudinal and Cross sectional detailing of full pavement width km 5.5 1.4 PROJECT SIGN BOARDS Imagement board Imagement provide and maintain Project sign board nr 2 1.5 INSURANCE Imagement board <	ITEM NO		DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT (Rs)	
1.1 TRAFFIC SAFETY & CONTROL Image: Control and Temporary Diversion of Traffic, including provision of a general traffic management plan month 9 1.1 103(1) and Temporary Diversion of Traffic, including provision of a general traffic management plan month 9 1.2 MOBILIZATION AND DEMOBILIZATION AND DEMOBILIZATION Image: Contractor's facilities and Plant / Equipment LS 1.2.1 P(001) Mobilization & De-Mobilization of Contractor's facilities and Plant / Equipment LS 1.3 SECTION SURVEYS AND DRAWINGS Image: Contractor's facilities and Plant / Equipment LS 1.3.1 117(1) Longitudinal and Cross sectional detailing of full pavement width km 5.5 1.4 PROJECT SIGN BOARDS Image: Contractor's facilities and Plant / Estimation Project sign or 2 Image: Contractor's facilities and Plant / Estimation Project sign or 2 1.4 PROJECT SIGN BOARDS Image: Contractor's facilities and Plant Project sign or 2 Image: Contractor's facilities and Plant Project sign or 2 1.5 INSURANCE Image: Contractor's facilities and Plant Project sign or 2 Image: Contractor's facilities and Plant Project sign or 2 1.5.1 119.1(1) Allow for the cost of providing all necessary Insurances Image: 2 Image: 2	Bill Pay							
1.1 Management, Safety and Control and Temporary Diversion of Traffic, including provision of a general traffic management plan month 9 1.2 MOBILIZATION AND DEMOBILIZATION month 9 1.2 MOBILIZATION AND DEMOBILIZATION LS 1.2.1 P(001) Mobilization & De-Mobilization of Contractor's facilities and Plant / Equipment LS 1.3 SETTING OUT,CROSS SECTION SURVEYS AND DRAWINGS LS SETTING OUT,CROSS 1.3.1 117(1) Longitudinal and Cross sectional detailing of full pavement width km 5.5 1.4 PROJECT SIGN BOARDS Image: Contractor's facilities and Plant Project sign board Image: Contractor's facilities and Plant Project sign board Image: Contractor's facilities and Plant Project sign board 1.4.1 118(1) Provide and maintain Project sign board Image: Contractor's facilities and Plant Project sign board Image: Contractor's facilities and Plant Project sign board 1.5.1 119.1(1) Allow for the cost of providing all necessary Insurances Image: Contractor's facilities and Plant Project sign board Image: Cont	BILL No	5.1 : Pl	RELIMINARY GENERAL					
1.1103(1)and Temporary Diversion of Traffic, including provision of a general traffic management planmonth91.2Mobilization AND DEMOBILIZATIONmonth91.2Mobilization & De-Mobilization of Contractor's facilities and Plant / EquipmentLS1.3SECTION SURVEYS AND DRAWINGSLS1.3.1117(1)Longitudinal and Cross sectional detailing of full pavement widthkm5.51.4PROJECT SIGN BOARDSImage: section of the cost of providing all necessary Insurancesnr21.5INSURANCEImage: section of the cost of providing all necessary InsurancestsImage: section of the cost of providing all necessary InsurancesBILL No.2: EARTH WORKSTrimming, Leveling and compaction of original ground to 100% STD.m²1,782.002.1304(3)Trimming, Leveling and compaction of original ground to 100% STD.m²1,782.00	1.1		TRAFFIC SAFETY & CONTROL					
I.2 DEMOBILIZATION 1.2.1 P(001) Mobilization & De-Mobilization of Contractor's facilities and Plant / Equipment I.S I.3 SETTING OUT, CROSS SECTION SURVEYS AND DRAWINGS I.S 1.3.1 117(1) Longitudinal and Cross sectional detailing of full pavement width km 5.5 1.4 PROJECT SIGN BOARDS Image: Contractor's for the cost of provide and maintain Project sign board nr 2 1.4.1 118(1) Provide and maintain Project sign board nr 2 1.5 INSURANCE Image: Contractor's for the cost of providing all necessary Insurances Image: Contractor's for the cost of providing all necessary Insurances Image: Contractor's for the cost of providing all necessary Insurances Image: Contractor's for the cost of providing all necessary Insurances Image: Contractor's for the cost of providing all necessary Insurances Image: Contractor's for the cost of providing all necessary Insurances Image: Contractor's for the cost of providing all necessary Insurances Image: Contractor's for the cost of providing all necessary Insurances Image: Contractor's for the cost of providing all necessary Insurances Image: Contractor's for the cost of providing all necessary Insurance Image: Contractor's for the cost of providing all necessary Insurance Image: Contractor's for the cost of providing all necessary Insurance Image: Contractor's for the cos	1.1 10)3(1)	and Temporary Diversion of Traffic, including provision of a general traffic management plan	month	9			
P(001)Mobilization & De-Mobilization of Contractor's facilities and Plant / EquipmentLS1.3SETTING OUT,CROSS SECTION SURVEYS AND DRAWINGSLS1.3.1117(1)Longitudinal and Cross sectional detailing of full pavement widthkm1.4PROJECT SIGN BOARDS1.4.1118(1)Provide and maintain Project sign boardnr21.5INSURANCE1.5.1119.1(1)Allow for the cost of providing all necessary InsurancesI.SBill No. 1 Carried to SummaryI.SBILL No.2: EARTH WORKS2.1304(3)Trimming, Leveling and compaction of original ground to 100% STD.m²2.2301(11)Roadway excavation , Unsuitablem³356.40	1.2							
1.3 SECTION SURVEYS AND DRAWINGS Image: mathematical symbol Image: mathematical symbol 1.3.1 117(1) Longitudinal and Cross sectional detailing of full pavement width km 5.5 1.4 PROJECT SIGN BOARDS Image: mathematical symbol Image: mathematical symbol Image: mathematical symbol 1.4.1 118(1) Provide and maintain Project sign board nr 2 Image: mathematical symbol 1.4.1 118(1) Provide and maintain Project sign board nr 2 Image: mathematical symbol 1.5.1 INSURANCE Image: mathematical symbol Image: mathematical symbol Image: mathematical symbol 1.5.1 119.1(1) Allow for the cost of providing all necessary Insurances Image: mathematical symbol Image: mathematical symbol BILL No.2: EARTH WORKS Image: mathematical symbol m² 1,782.00 Image: mathematical symbol Ima	1.2.1 P((001)	Mobilization & De-Mobilization of Contractor's facilities and Plant / Equipment	LS				
1.3.1 117/(1) detailing of full pavement width km 5.5 1.4 PROJECT SIGN BOARDS nr 2 1.4.1 118(1) Provide and maintain Project sign board nr 2 1.5 INSURANCE 1 119.1(1) Allow for the cost of providing all necessary Insurances LS 1.5.1 119.1(1) Allow for the cost of providing all necessary Insurances LS 1 Bill No. 1 Carried to Summary LS 1 1 1 BILL No.2: EARTH WORKS Trimming, Leveling and compaction of original ground to 100% STD. m² 1,782.00 2.1 304(3) Roadway excavation , Unsuitable m³ 356.40	1.3		SECTION SURVEYS AND					
1.4.1 118(1) Provide and maintain Project sign board nr 2 1.5 INSURANCE 1 119.1(1) Allow for the cost of providing all necessary Insurances I.S I.S Bill No. 1 Carried to Summary I.S I.S I.S I.S Bill No. 1 Carried to Summary I.S I.S I.S I.S 2.1 304(3) Trimming, Leveling and compaction of original ground to 100% STD. m ² 1,782.00 2.2 301(11) Roadway excavation , Unsuitable m ³ 356.40	1.3.1 11			km	5.5			
1.4.1118(1)boardnr21.5INSURANCE $1.5.1$ INSURANCE $1.5.1$ $119.1(1)$ Allow for the cost of providing all necessary Insurances 1.5 BILL No. 1 Carried to SummaryBILL No.2: EARTH WORKS2.1 $304(3)$ Trimming, Leveling and compaction of original ground to 100% STD. m^2 $1,782.00$ 2.2 $301(11)$ Roadway excavation , Unsuitable m^3 356.40	1.4		PROJECT SIGN BOARDS					
1.5.1 119.1(1) Allow for the cost of providing all necessary Insurances LS Image: Compact of Com	1.4.1 11	18(1)		nr	2			
I.S.1 IT9.1(1) necessary Insurances LS Bill No. 1 Carried to Summary Image: Second State St	1.5		INSURANCE					
BILL No.2: EARTH WORKS 2.1 304(3) Trimming, Leveling and compaction of original ground to 100% STD. m ² 1,782.00 2.2 301(11) Roadway excavation , Unsuitable m ³ 356.40	1.5.1 119	9.1(1)		LS				
2.1 304(3) Trimming, Leveling and compaction of original ground to 100% STD. m ² 1,782.00 2.2 301(11) Roadway excavation , Unsuitable m ³ 356.40	Bill No. 1	Carri	ed to Summary					
2.1 $304(3)$ compaction of original ground to 100% STD. m^2 $1,782.00$ 2.2 $301(11)$ Roadway excavation, Unsuitable m^3 356.40	BILL No	э.2: ЕА	ARTH WORKS					
$-2_{1}2_{2} + 3_{1}1_{1} + 1_{2}1_{2} + 1_{2}$	2.1 30)4(3)	compaction of original ground to 100% STD.	m ²	1,782.00			
	2.2 301(11) Roadway excavation, Unsuitable		m ³	356.40				
Bill No. 2 Carried to Summary	Bill No. 2	2 Carri	ed to Summary					
BILL No.3 : SUB BASE, BASES AND SHOULDERS	BILL No	5. 3 : S I	UB BASE, BASES AND SHOULD	ERS				
3.1 405(1) Dense graded aggregate base (Base m ³ 392.04	3.1 40)5(1)		m ³	392.04			
3.2 409(1) Earthen shoulder as compacted in m^3 1,100.00	3.2 40)9(1)	1	m ³	1,100.00			
	Bill No. 3	8 Carri	ed to Summary					

RECTIFICATION AND ASPHALT SURFACING ON AMPARA-IGNIYAGALA ROAD (11+500-

17+000) KM

ITE	EM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT (Rs)	
Bill Pay		DESCRIPTION	UNII	QUANTITI	KATE	AMOUNT (KS)	
BILI	L No.4 : SI	URFACE APPLICATION AND S	URFACIN	NGS			
	4.1 PRIME COAT AND TACK COAT						
4.1.1	501(5)	Bituminous Prime Coat using CSS -1 at 1 litre per m ²	m ²	1,782.00			
4.1.2	502(2)	Bituminous Tack Coat (CSS1 at 0.5 litre/m2)	m ²	35,640.00			
	4.2	BITUMINOUS SURFACING					
4.2.1	506(2)	Asphalt concrete in binder/ Correction course	МТ	577.37			
4.2.2	506(1)	Asphalt concrete in wearing course 40mm compacted thickness	m ²	29,700.00			
Bill N	Bill No. 4 Carried to Summary						
BILI	BILL No.5: INCIDENTAL WORKS						
	5.1	ROAD MARKING					
		Edge line :					
5.1.1	810(1)	Continuous	m ²	1,100.00			
5.1.2	810(1)	Pedestrian crossing	m ²	150.00			
5.2 ROAD SIGNS							
		Reflective road sign :					
5.2.1	811(1)	Single pole, sign area up to 0.5m ²	nr	20.00			
5.2.2	811(2)	Double pole, sign area up to 2.0m ²	nr	5.00			
5.2.3	811(3)	Chevron warning sign	nr	24.00			
Bill No. 4 Carried to Summary							
	Ş						

RECTIFICATION AND ASPHALT SURFACING ON AMPARA-IGNIYAGALA ROAD (11+500-17+000) KM

BILL No.6 : SCHEDULE OF DAY WORKS RATES

6.1: LABOUR DAY WORKS

All Quantities are Provisional

	ATE	AMOUNT (Rs)
-		

SECTION - 9

SCHEDULES

ITB Clause	nture partners, each partner shall fu	Information				
Reference	Description	To be filled by Bidder	Remarks			
	CIDA Registration		Provide certified copies			
	Registration Number		and label as attachment			
	Grade		to Clause 3.1			
3.1	Specialty					
	Expiry Date					
	Number					
	Expiry Date					
4.1(a)	Legal Status		Provide certified copies o			
412(0)			registration			
	Written power of attorney to the	Provide original or certified copy of the power of				
	signatory to the bid (bids signed by	attorney attested by a Notary and label as				
	other than the authorized person,	attachment to Clause 4.1(a)				
	shall be rejected)					
	If a Joint Venture, names and	1	Provide draft copy of Join			
	addresses of Joint Venture partners	2	Venture agreement			
		3				
	If a Joint Venture, name of the Lead		1			
	Partner					
	For Joint Ventures, each JV partner shall furnish legal status separately					
	Name (lead partner)		Provide certified copies			
	Legal status		and label as attachment t			
	Place of registration		Clause 4.1(a)			
	Principal place of business					
	Written power of attorney of the	Provide original or cert	ified copy of the power of			
×	signatory to the Bid	attorney attested by a	Notary and label as			
		attachment to Clause 5	5.1			
	VAT Registration No.					
	Name (Partner 2)		Provide certified copies			
	Legal status		and label as attachment t			
	Place of registration		Clause 4.1(a)			
	Principal place of business		1			

Written power of attorney of the	Provide original or cer	tified copy of the power of	
signatory to the Bid	attorney attested by a	Notary and label as	
	attachment to Clause 5.1		
VAT Registration No.			
Name (Partner 3)		Provide certified copies and	
Legal status		label as attachment to	
 Place of registration		Clause 4.1(a)	
Principal place of business			
Written power of attorney of the	Provide original or cer	tified copy of the power of	
signatory to the Bid	attorney attested by a Notary and label as attachment to Clause 5.1		
VAT Registration No.			

Schedule 2 – Annual Turnover Ini	ormation	
For Joint Ventures each partner s		eparately
Year	Turnover	Remarks
2022/2023		Attach certified copy of audited reports and label as attachment to
2021/2022		Clause 4.2
2020/2021		
2019/2020		
2018/2019		

Schedule 3 – Adequacy of Working Source of Credit Line	Amount	Remarks			
		Provide documentary evidence and label as attachment to Clause 4.2			
Total					

	Financial Data st Audited Financial Statement)	2019/2020 or latest
1	Current Assets	
2	Current Liabilities	
3	Working Capital(1-2)	
4	Works in hand	
5	Line of credit**	
6	Available Liquid Asset {3-(0.1)x4+5}*	

* This amount shall be not less than the amount given in clause 4.2 of ITB.

** Available Working capital of the bidder should be positive (+)

*** Line of credit if provided shall strictly be as per Form No. 07 provided.

	-	ice in last ten years information separately	\bigcirc	/
Year	Employer	Description of Works	Amount	Contractors Responsibility (%)

Schedule 6 – Major Items of C	onstruction Equipment Propo	osed
Туре	Capacity	Own, Lease or hire

A: Key Professional		
Name	Position	Task
B: Support Staff		
Name	Position	Task

			Sche	dule	I ∞	Time	Sch	equi	e fo	or Ke	Schedule 8 – Time Schedule for Key Staff	Ħ					
~		R						Ma	onths	s(in tł	Je forn	n of a l	Months(in the form of a Bar Chart)	t)			
Name	Position	Activities	1 2 3	4		5 6	2	8	6	10	11	12				Number of Months	s
			¢		7.)												
Full Time:-				Ğ	art Ti	Part Time:]

Schedule No. 09 (a) Non-Performance Contracts – Notice to

Correct Issued

[The following table shall be filled in for the bidder and for each partner of a Joint Venture]

Date: Contract No.: Bidder's Legal Name: Page _____ of

1. History of Non Performing Contracts - Notice to Correct Issued

	Non-Performing Contracts						
N is B N is	inforced prior to idding Data, sub lotice to Correct o	n the poor performance or similar notice as per the re June 19, 2024 has not been issued as specified is clause 4.2 (h) n the poor performance or similar notice as per the re June 19, 2024 has been issued as specified in S	in Section II, levant COC, which				
Year	Non Performed Portion of Contract	Contract Identification	Total Contract Amount (LKR)				
[insert year]	[insert amount and percentage]	Contract Identification: [indicate complete contract name, number, and any other identification] Name of Employer: [insert full name] Address of Employer: [insert street/city/country] Reason(s) for Notice to Correct: [indicate main reason(s), attach copy of Notice to Correct] Whether Remedies taken: (Yes/No) (If yes, attach Engineer's certificate) Current Status of Contract: (indicate completed/ongoing/ referred to dispute resolution	[insert amount]				

••••••

Signature of the Bidder

Attorney at Law

Note – if does not provide all non performing contracts shall be treated as non - responsive according to the clause 3.3 of ITB

Schedule No. 09 (b) Non-Performance Contracts – Terminated

[The following table shall be filled in for the bidder and for each partner of a Joint Venture]

Date:	
Contract No.:	
Bidder's Legal Name:	
Bidder's Party Legal Nam	ne:

1. History of Non Performing Contracts - Terminated Contracts

Non-Performing							
		Contracts					
Choose o	ne of the followin	g					
(5)	years prior to June mination of Contra	acts due to the Contractor's default did not occu e 19, 2024 specified in Section II, Bidding Data, s acts due to the Contractor's default occurred withi specified in Section II, Bidding Data, sub clause 4.2	ub clause 4.2 (h) n last five (5) years				
Year	Non Performed Portion of Contract (Rs)	Contract Identification	Total Contract Amount (LKR)				
[insert year]	[insert amount and percentage]	Contract Identification: [indicate complete contract name, number, and any other identification] Name of Employer: [insert full name] Address of Employer: [insert street/city/country] Reason(s) for non-performance/termination: [indicate main reason(s), attach relevant details] Current Status of Contract: (indicate completed/ongoing/ referred to dispute resolution	[insert amount]				

Cignature of the Biddor

Signature of the Bidder

.....

Attorney at Law

Note - if does not provide all non performing contracts shall be treated as non - responsive according to the clause 3.3 of ITB

Schedule No. 10 Pending Litigation and Arbitration

Each Bidder must fill out this form if so required under Criterion 4.2 (i) of Section 2, Bidding Data to describe any pending litigation or arbitration formally commenced against it.

In case of a Joint Venture, each Joint Venture Partner must fill out this form separately and provide the Joint Venture Partner's name below:

Joint Venture Partner: _____

		Pending L	itigation and Arbitration	4
Choose on	e of the following			
		of all pending liti	n accordance with section II, Biddin gation and arbitration in accordance ta, sub clause 4.2 (i)	
Year of	Amount of	Outcome as	Contract Identification	Total Contract
Dispute	Dispute	percentage of Net worth		Amount
			Contract Identification (insert contract name, number and any other identification) Name of Employer (insert full name) Address of Employer (insert street, city, town) Matter in dispute (indicate main issues in dispute) Status of dispute (indicate if it is being treated by the adjudicator, under arbitration or being dealt with by the judiciary)	

.....

Signature of the Bidder

Attorney at Law

Note – if does not provide all pending litigation arbitration shall be treated as non responsive according to the clause 3.3 of ITB

	: Date)						
	$(1^{st}$, 2^{nd} etc. are months from the Start Date)	11 th 12 th					
	months frc	10 th			2)		
	etc. are	8t h 9th		\bigcirc			
	1 st , 2 nd	$7^{ m th}$					
		5 th 6 th	R				
		4 th 5					
		3 rd					
a		2 nd					
gramm		1 st					
Schedule 11 – work Programme		Construction Activity					

SECTION - 11

STANDARD FORMS (BID)

FORM NO. 06: Form of Bid Security FORM NO. 07: Form for the Affidavit for the Current Contractual Commitments FORM NO. 08: For Letter from the Bank for Granting of A Revolving Line of Credit

FORM OF BID SECURITY

[this Guarantee form shall be filled in accordance with the instructions indicated in brackets]

......[insert issuing agency's name, and address of issuing branch or office]

Beneficiary: Director General, Road Development Authority, "MagaNeguma Mahamedura" 216, Denzil Kobbekaduwa mawatha, Battaramulla, Sri Lanka.

Date:[insert (by issuing agency) date]

BID GUARANTEE No.:[insert (by issuing agency) number]

We have been informed thatinsert (by issuing agency) name of the Bidder] (hereinafter called "the Bidder") has submitted to you its bid dated[insert (by issuing agency) date] (hereinafter called "the Bid") for the execution of execute 'RECTIFICATION AND ASPHALT SURFACING ON AMPARA IGINIYAGALA ROAD FROM 11+500 TO 17+000 KM' under Contract No: RDA/RM&M/EP(Akk)/RMI/2024/13

Furthermore, we understand that, according to your conditions, Bids must be supported by a Bid Guarantee.

At the request of the Bidder, we*[insert name of issuing agency]* hereby irrevocably undertake to pay you any sum or sums not exceeding in total an amount of*[insert amount in figures]**[insert amount in words]* upon receipt by us of your first demand in writing accompanied by a written statement stating that Bidder is in breach of its obligation(s) under the bid conditions, because the Bidder:

- i. has withdrawn its Bid during the period of bid validity specified; or
- ii. does not accept the correction of errors in accordance with the Instruction to Bidders (hereinafter "the ITB") of the IFB or
- iii. having been notified of the acceptance of its Bid by the Employer during the period of bid validity,
 - (i) fails or refuses to execute the Contract Form, if required, or
 - (ii) fails or refuses to furnish the Performance Security, in accordance with the ITB.

This Guarantee shall expire:

- (a) if the Bidder is the successful bidder, upon our receipt of copies of the Contract signed by the Bidder and of the Performance Security issued to you by the Bidder; or

Consequently, any demand for payment under this Guarantee must be received by us at the office on or before that date.

Signature and the Seal of the Guarantor: Name of the Organization Date: Witness:

Note: Any bid security which has deviated from this bid Security format shall be considered as non responsive

FORM FOR THE AFFIDAVIT FOR THE CURRENT CONTRACTUAL COMMITMENTS

Chairman,

Road Development Authority Procurement Committee.

Specialty	Name of the Contract	Name of the Client	Initial Contract Amount (Rs.)	Outstanding Work (Rs.)
Highways*				
Bridges*				
Buildings*		C		
Irrigation*				
#				
	(C, \mathcal{O})			
	Т	otal		

.....

Signature of the Bidder

Justice of The Peace

* Add additional rows to include all the current projects if needed

Add additional speciality to include all the current projects

Note - if does not provide all contract commitment shall be treated as non responsive according to the clause 3.3 of ITB

FOR LETTER FROM THE BANK FOR GRANTING OF A REVOLVING LINE OF CREDIT

FROM	:	
то	:	Director General,
		Road Development Authority (RDA)
		"MagaNeguma Mahamedura " 216, Denzil Kobbekaduwa mawatha,
		Battaramulla
		Sri Lanka
SUB	:	Letter from the Bank for providing a line of credit in favour
		of (1) in case of award to them of works for the
		Contract of execute RECTIFICATION AND ASPHALT SURFACING ON
		AMPARA IGINIYAGALA ROAD FROM 11+500 TO 17+000 KM, under
		contract No: RDA/RM&M/EP(Akk)/RMI/2024/13
Dear S	ir,	
	We (2)	hereby agree to grant revolving line
		mount of Sri Lanka Rupees for the purpose of the execution of
		contracts under the Contract of execute RECTIFICATION AND ASPHALT
		AMPARA IGINIYAGALA ROAD FROM 11+500 TO 17+000 KM Contract No:
		Akk)/RMI/2024/13. This revolving line of credit will be maintained until the
	works are taken o	
U	and the Seal of the	
	ie Organization	
Notes	/	
(1)	Name of Bene	ficiary / Bidder
(2)	Name of Bank	
(3)	Name of Bene	ficiary / Bidder
(4)		line of credit will be accepted and any letter of line of credit, which has deviated men format, shall be treated as non – responsive.

